

## **Daily Report**

Tuesday, Sep 03, 2024

## **Sheridan County Brooks Street Greenspace**

224 South Main Street Sheridan, WY 82801 Job#: 6017.002.00

#### LANDSCAPE IMPROVEMENTS

11:35 AM Tre LaBossiere

[Lat/Long: 44.795266,-106.957444]

Arrived on site at 11 for the weekly construction meeting.

Following the meeting Nathan Steiner was on site to discuss the plantings layout with Highland Inc. Nathan moved plants around and discussed with highland the appropriate locations for each plant. Highland will work on getting all of these planted following Nathan approving the locations.

Westin was on site but was not currently working. They were waiting to hear back from Ryan Thompson (M-M Mechanical) for more guidance/clarification on the spacing limitation for the heat tubing under the pergola pad.

NU was not actively working on site.





Tre LaBossiere: Ju LaBossive



# **Daily Report**

## Thursday, Sep 05, 2024

## **Sheridan County Brooks Street Greenspace**

224 South Main Street Sheridan, WY 82801 Job# : 6017.002.00

#### LANDSCAPE IMPROVEMENTS

#### 02:03 PM Tre LaBossiere


[Lat/Long: 44.794019,-106.946079]

Arrived on site at 2:30 on 9/4. There was no work happening on site. Highland was on site and was able to spread the landscaping rock over the freshly planted area just west of walls two and four.

Westin had placed some insulation and reinforcing on the sidewalk where Stonemill had already formed. Westin had also placed more tubing over the areas that didn't have heat tubing yet.





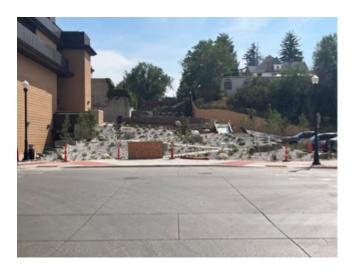

Tre LaBossiere: The LaBossiere



# **Daily Report**

Friday, Sep 06, 2024

## **Sheridan County Brooks Street Greenspace**

224 South Main Street Sheridan, WY 82801 Job# : 6017.002.00

#### **MECHANICAL IMPROVEMENTS**

#### 02:53 PM Tre LaBossiere

[Lat/Long: 44.781868,-106.940259]

Arrived on site at 2:30. No work was in progress when I arrived on site. Weston laid down the tubing for the sidewalk for the rest of snowmelt zone three. There were no issues with how Weston laid down the tubing all appeared to be satisfactory according to the specifications.







Tre LaBossiere: Tu LaBossiere
