

SHERIDAN COUNTY – BROOKS STREET GREENSPACE

CHANGE ORDER

No. 1 DATE OF ISSUANCE: 9/13/2023
PROJECT: Brooks Street Greenspace EFFECTIVE DATE: 9/13/2023
OWNER: Sheridan County OWNER's Contract No.: _____
CONTRACTOR: Northern Underground ENGINEER: Morrison-Maierle
TO: Northern Underground, LLC DATE OF CONTRACT: June 6, 2023

You are directed to make the following changes in your Contract for the above project. These changes are made in accordance with the General Conditions of this contract.

Description of changes:

- Additional 30 Calendar Days and an additional \$66,645.00 in price were added to the contract.
 - o Revised Contract Days: **220 Calendar days**
 - o Revised Contract Price: **\$2,308,784.15**

Reason for Change Order:

The owner requested the abandonment of the existing waterline in Brooks St after evaluation of the line by the City of Sheridan and new services be installed to both the Sheridan County Juvenile Justice building and County Courthouse.

Attachments:

- Waterline plan and profile sheet
- Northern Underground proposal
 - o Proposal mentions additional dollars for heating/covering concrete in cold temperatures. If needed, this will be handled with the Miscellaneous Additional Work bid item.

CHANGE IN CONTRACT PRICE:

Original Contract Price \$ 2,242,139.15

Net Changes from Previous Change Orders
No. 0 to No. 1

\$ \$66,645.00

CHANGE IN CONTRACT TIME:

Original Contract Time 190 Calendar days

Substantial Completion: October 31, 2024

Final Completion: 14 Calendar Days

Net change from previous Change Orders
No. 0 to No. 1

30 Calendar Days
days

SHERIDAN COUNTY – BROOKS STREET GREENSPACE

Contract Price prior to this Change Order

\$ 2,242,139.15

Net Increase (~~decrease~~) of this Change Order

\$ 66,645.00

Contract Price with all approved Change Orders
(including this one):

\$ 2,308,784.15

Contract Times Prior to this Change Order

Substantial Completion: Oct 31, 2024

Final Completion: 14 calendar days
days or date

Net Increase (~~decrease~~) of this Change Order

30 calendar days
days

Contract Times with all approved Change
Orders (including this one):

Substantial Completion: Nov 30, 2024

Final Completion: 14 calendar days
days or date

CONTRACTOR:

By: 

Title: Manager

Date: 9/13/23

ENGINEER:

By: 

Title: Project Manager


Date: 9/13/2023

SHERIDAN COUNTY:

By: 

Title: Chairwoman

Date: 09/19/23

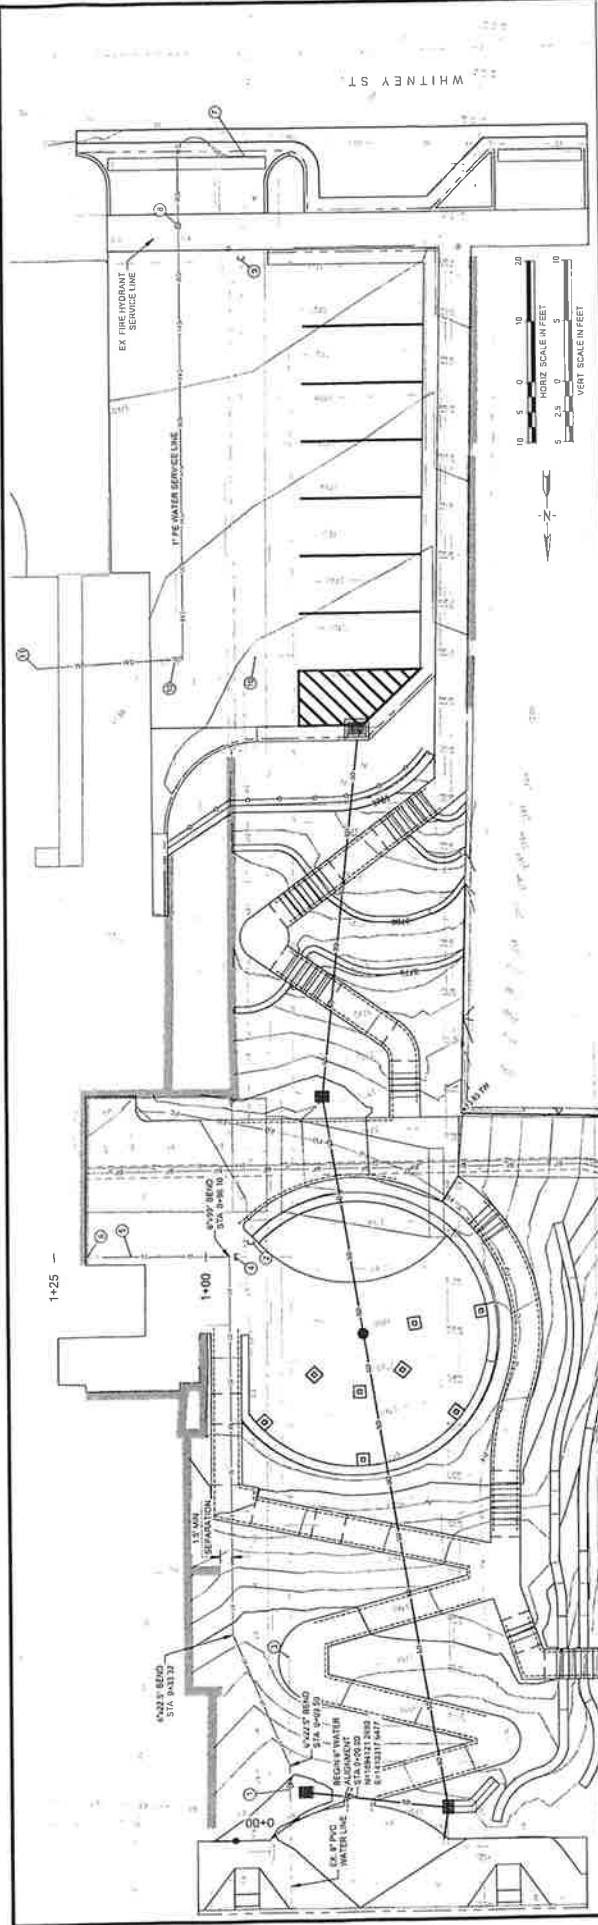



Itemized Proposal

Wednesday, September 13, 2023

PR # 01

PROJECT: Brooks Street

OWNER: Sheridan County

TO: Tim Brugger

FROM: Aaron

Listed below is an itemized description for the extra work

Item	Quantity	Describe Work, Materials, or Labor	Unit Price	Ext. Price
		6" Service		
1	2	Connect to existing main and to building	\$ 5,800.00	\$ 11,600.00
2	115	LF, 6" main	\$ 65.00	\$ 7,475.00
3	1	Valve	\$ 2,200.00	\$ 2,200.00
4	3	Fittings	\$ 1,500.00	\$ 4,500.00
5	2	Cap Existing Main @ note 2 & 4	\$ 1,200.00	\$ 2,400.00
6	1	Hard surfacing	\$ 6,600.00	\$ 6,600.00
7	1	Remove existing valve and plug pipe @ note 3	\$ 2,000.00	\$ 2,000.00
8	1	Chlorination, flushing and NAFP24 testing	\$ 4,000.00	\$ 4,000.00
			TOTAL	\$ 40,775.00
		1" Service		
1	1	Tap main w/ corp and saddle	\$ 7,500.00	\$ 7,500.00
2	121	LF, 1" HDPE service w/ HDD	\$ 70.00	\$ 8,470.00
3	1	Curb stop	\$ 400.00	\$ 400.00
4	1	Connect to service inside building	\$ 6,500.00	\$ 6,500.00
5	1	Cap existing main @ note 9	\$ 2,000.00	\$ 2,000.00
6	1	Chlorination and flushing	\$ 1,000.00	\$ 1,000.00
			TOTAL	\$ 25,870.00
		Daily rate to heat and cover delayed concrete pours	\$ 1,000.00	

Additional Time of 30 days will be added to the Contract Schedule to accommodate this Proposal Request.
